



# **BCSD GRANT WOOD ELEMENTARY SCHOOL**


## **MILESTONE & SCHEDULE UPDATE**

**MARCH 20, 2017**

# ADVOCATES

FROM CONCEPT TO COMPLETION

# BCSD GRANT WOOD ES: PRELIMINARY SCHEDULE

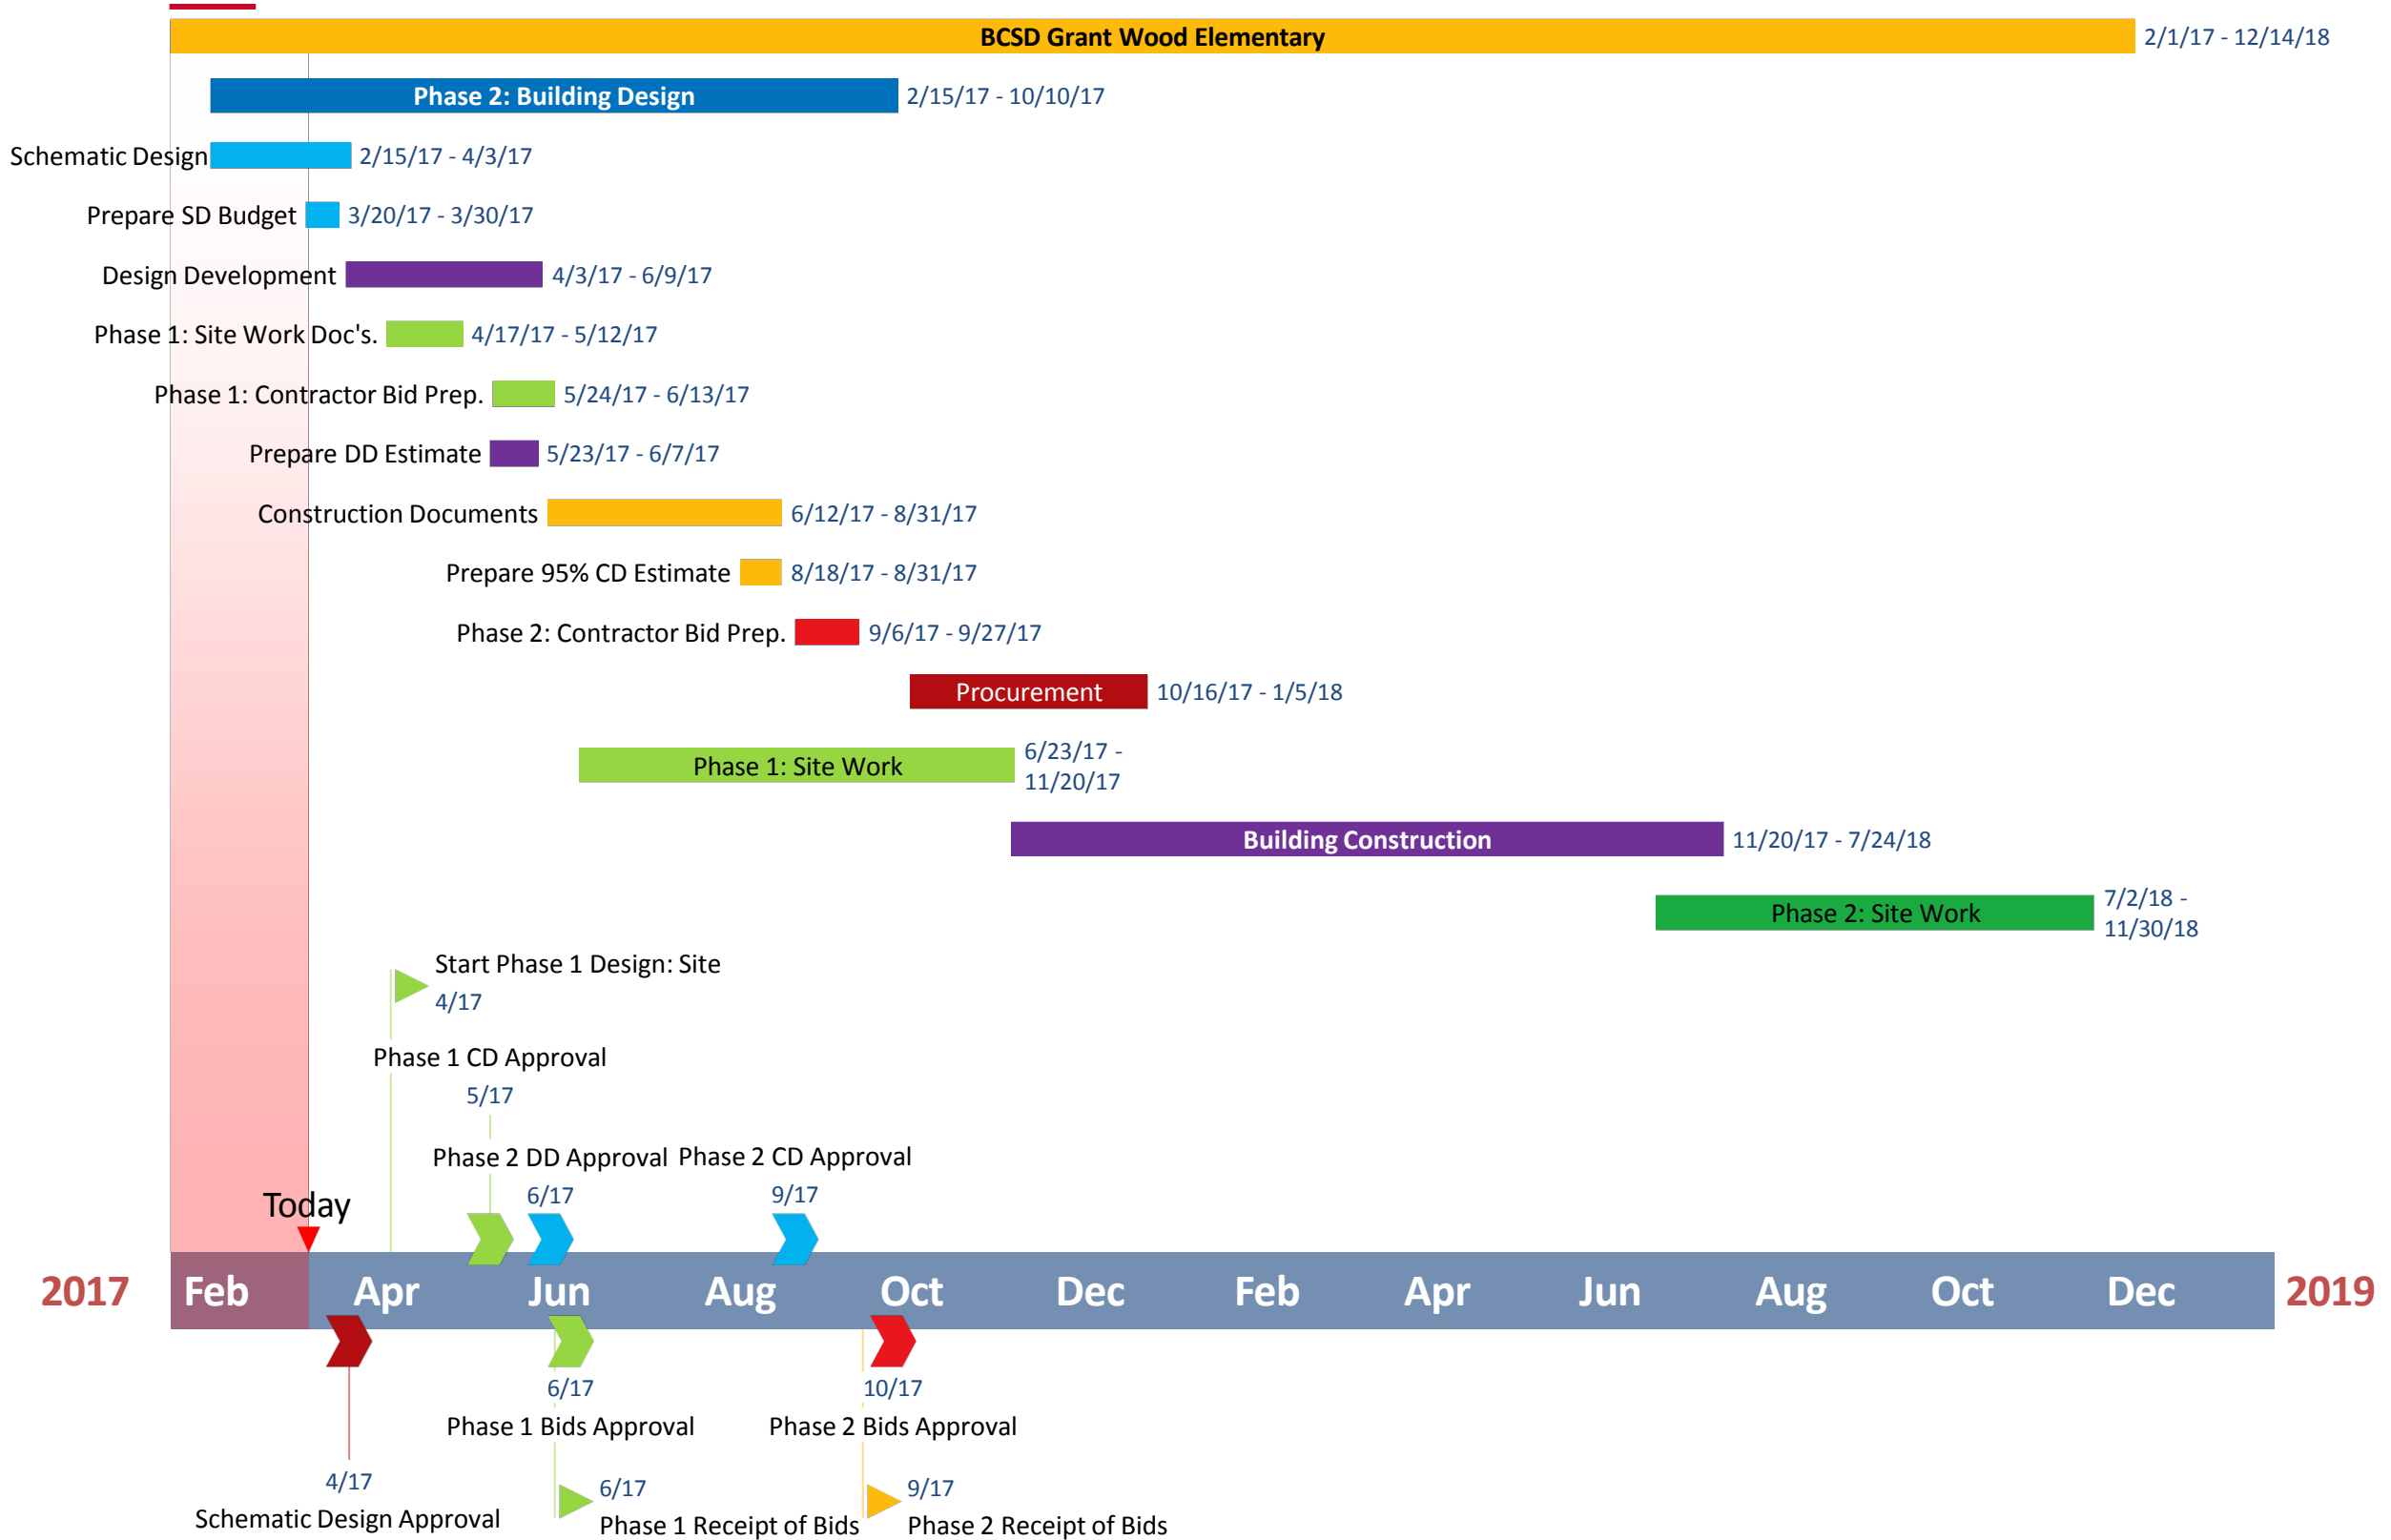

# BCSD GRANT WOOD ES: PRELIMINARY SCHEDULE



Milestone(s)	
Date	Description
04/03/2017	SD Approval
04/17/2017	Start Phase 1 Design: Site
05/22/2017	Phase 1 CD Approval
06/12/2017	Phase 2 DD Approval
06/13/2017	Phase 1 Receipt of Bids
06/19/2017	Phase 1 Bids Approval
09/05/2017	Phase 2 CD Approval
09/28/2017	Phase 2 Receipt of Bids
10/09/2017	Phase 2 Bids Approval

Task(s)			
Duration (days)	Start Date	End Date	Description
682	02/01/2017	12/14/2018	BCSD Grant Wood Elementary
238	02/15/2017	10/10/2017	Phase 2: Building Design
48	02/15/2017	04/03/2017	Schematic Design
11	03/20/2017	03/30/2017	Prepare SD Budget
68	04/03/2017	06/09/2017	Design Development
26	04/17/2017	05/12/2017	Phase 1: Site Work Doc's.
21	05/24/2017	06/13/2017	Phase 1: Contractor Bid Prep.
16	05/23/2017	06/07/2017	Prepare DD Estimate
81	06/12/2017	08/31/2017	Construction Documents
14	08/18/2017	08/31/2017	Prepare 95% CD Estimate
22	09/06/2017	09/27/2017	Phase 2: Contractor Bid Prep.
82	10/16/2017	01/05/2018	Procurement
151	06/23/2017	11/20/2017	Phase 1: Site Work
247	11/20/2017	07/24/2018	Building Construction
152	07/02/2018	11/30/2018	Phase 2: Site Work
